


Compressure Machine Checklist

Ref No.: PI/EHS/C/49
 Issue date: 05/05/25
 Rev No: 00

Inspection Information

Name of Site/Location	Animas	Frequency	Fortnite
Name Of Contractor	Universal	Responsible for checks	SO - gautham
Date of First Deployment	3/2/2026 1:50:27 PM	Checked by & date during site EHS Risk Evaluation	So - Lakshman 3/17/2026 1:50:27 PM
Date of Inspection	18-Mar-2026 07:56:30 PM	Machine Serial No:	9346832qgbd

Inspection Type Attachment

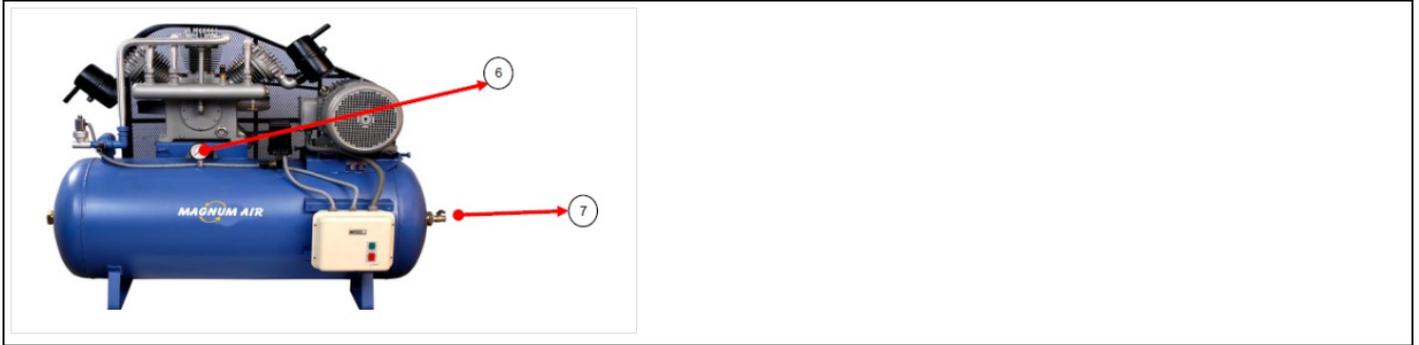

Checklist

Description	Yes	No	N/A	Observation Details
1.Tag or identification number of Air Compressor.	Yes			Report Compressure Machine Checklist 1
2.Valid Test certificate Available	Yes			Report Compressure Machine Checklist 2
3.Safety guards are in place				Report Compressure Machine Checklist 3
4.Hoses been held firmly with clips / clamps	Yes			Report Compressure Machine Checklist 4
5.Are there any damage / leak in the hoses?				Report Compressure Machine Checklist 5
6.Whether the pressure gauges show the correct working pressure?	Yes			Report Compressure Machine Checklist 6
7.Does the safety valve /air release at the set pressure?				Report Compressure Machine Checklist 7
8.Does the moisture drain valve in the air cylinder functions well?		No		Report Compressure Machine Checklist 8
9.Are the hose joints/sockets (Male/Female) properly engaged?	Yes			Report Compressure Machine Checklist 9
10.Is there any visible crack in the air receiver?			N/A	Report Compressure Machine Checklist 10
11.Is there leakage of diesel/ oil from machine?	Yes			Report Compressure Machine Checklist 11
12.Whether the compressor starts properly?	Yes			Report Compressure Machine Checklist 12

Overall Observation

Acceptable (Yes/No): No	If not acceptable - Equipment removed from site(Date) : 31-Jan-2026	Corrective/Preventive action taken on (Date) : 10-Mar-2026
--------------------------------	---	--

Inspection History

Created On	Created By	Comment	Attachments
18-Mar-2026 07:58:03 PM	Hebert Eaton	Hebert Eaton has Verified.	
